


This chart illustrates DoDI 5000.02, Hybrid Program Model A (Hardware Dominant); tailoring is encouraged.

# Defense Acquisition Life Cycle Objectives & Contributions with Tailoring

## Acquisition Milestones, Phases and Decision Points

These decision points and milestones are standard elements of the Defense Acquisition System. MDAs, with PM input, have full latitude to tailor programs to be effective and efficient, unless constrained by statute

For a complete list of statutory and regulatory information requirements, see Table 2, Encl 1, DoDI 5000.02

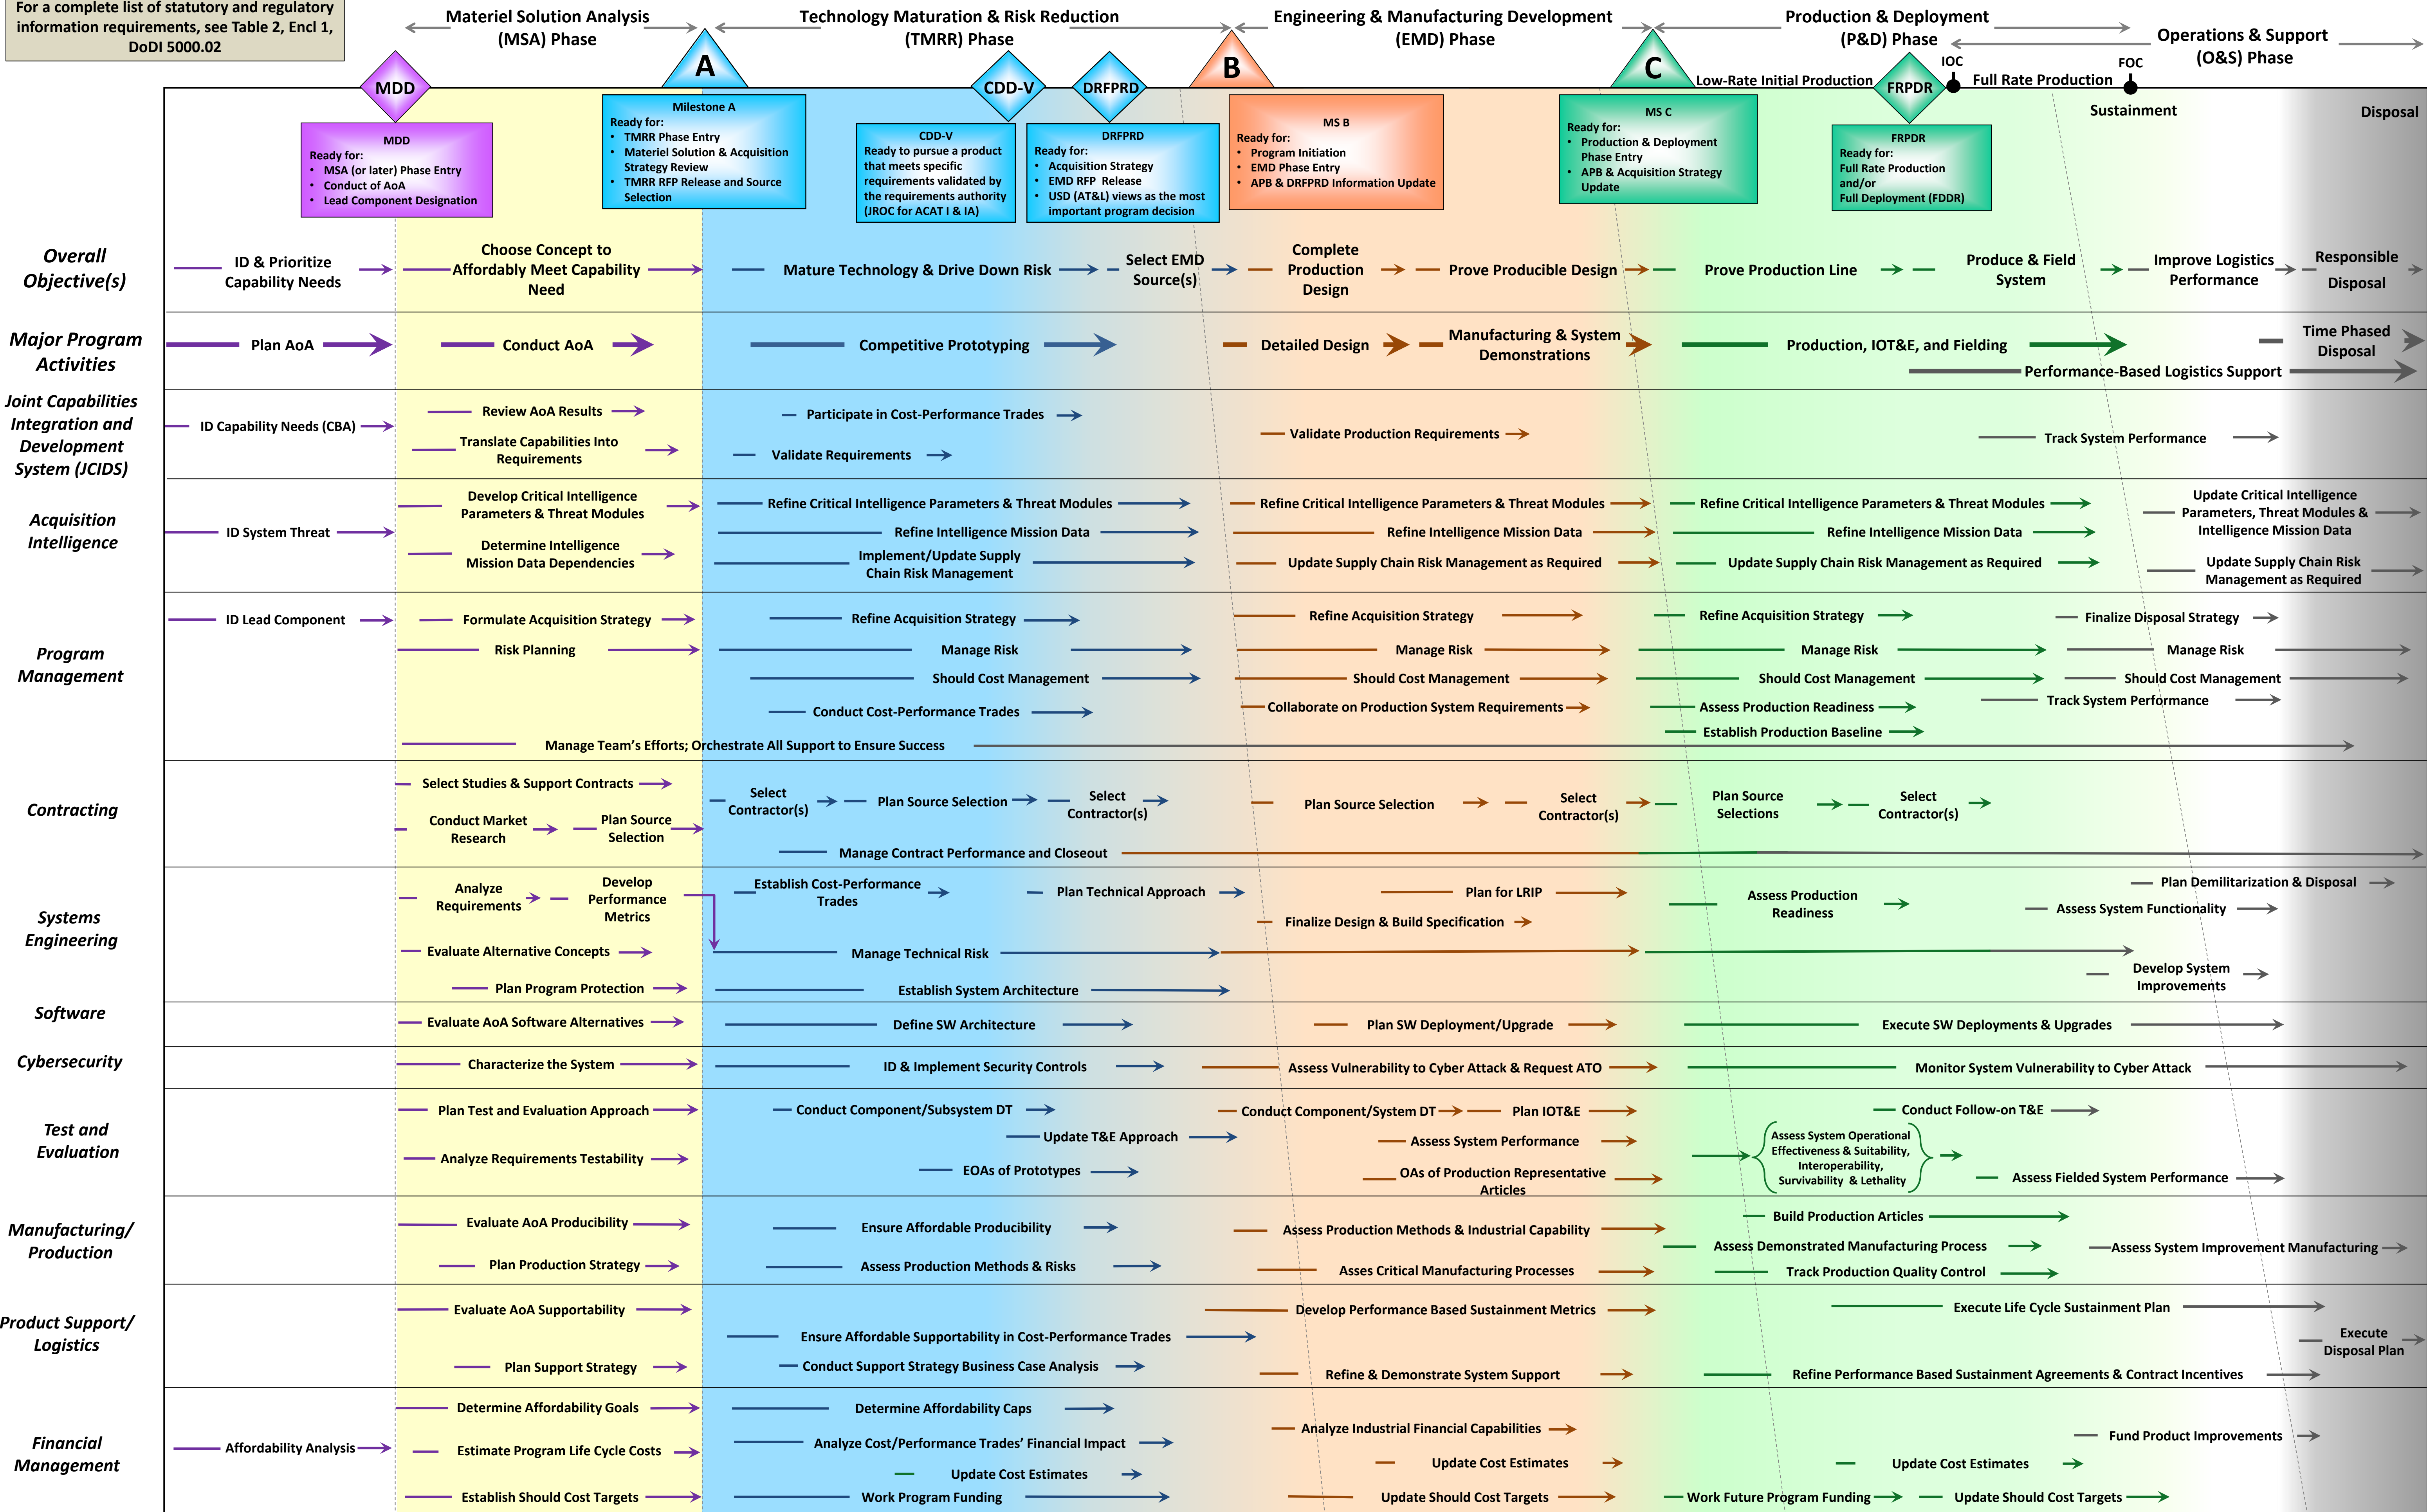

### Acronyms & Abbreviations

- ACAT – Acquisition Category
- APB – Acquisition Program Baseline
- AoA – Analysis of Alternatives
- CBA – Capabilities-Based Assessment
- CDD-V – Capability Development Document Validation
- DT – Developmental Testing
- DRFPRD – Development Request for Proposal Release Decision
- EMD – Engineering & Manufacturing Development
- FD – Full Deployment
- FRP – Full-Rate Production
- ID – Identify
- IOC – Initial Operational Capability
- IOT&E – Initial Operational Test & Evaluation
- FOC – Full Operational Capability
- JROC – Joint Requirements Oversight Council
- LRIP – Low-Rate Initial Production
- MDD – Materiel Development Decision
- MS – Milestone
- MSA – Materiel Solution Analysis
- OA – Operational Assessment
- O&S – Operations and Support
- P&D – Production and Deployment
- RFP – Request for Proposal
- SW – Software
- T&E – Test and Evaluation
- TMRR – Technology Maturation & Risk Reduction
- USD(AT&L) – Under Secretary of Defense (Acquisition, Technology & Logistics)



# Defense Acquisition Life Cycle Compliance with Tailoring


This chart illustrates DoDI 5000.02, Hybrid Program Model A (Hardware Dominant); tailoring is encouraged.

## Acquisition & Procurement Milestones, Phases and Decision Points

**Milestone & Phase Information Requirements**

Statutory information requirements are shown in dark red bold italics. Regulatory and best practice information requirements are shown in blue bold. For a complete list of statutory and regulatory information requirements see Table 2 of DoDI 5000.02

These decision points, milestones and phases are standard elements of the Defense Acquisition System; however, MDAs, with PM input, have full latitude to tailor programs in the most effective and efficient structure possible, unless constrained by statute

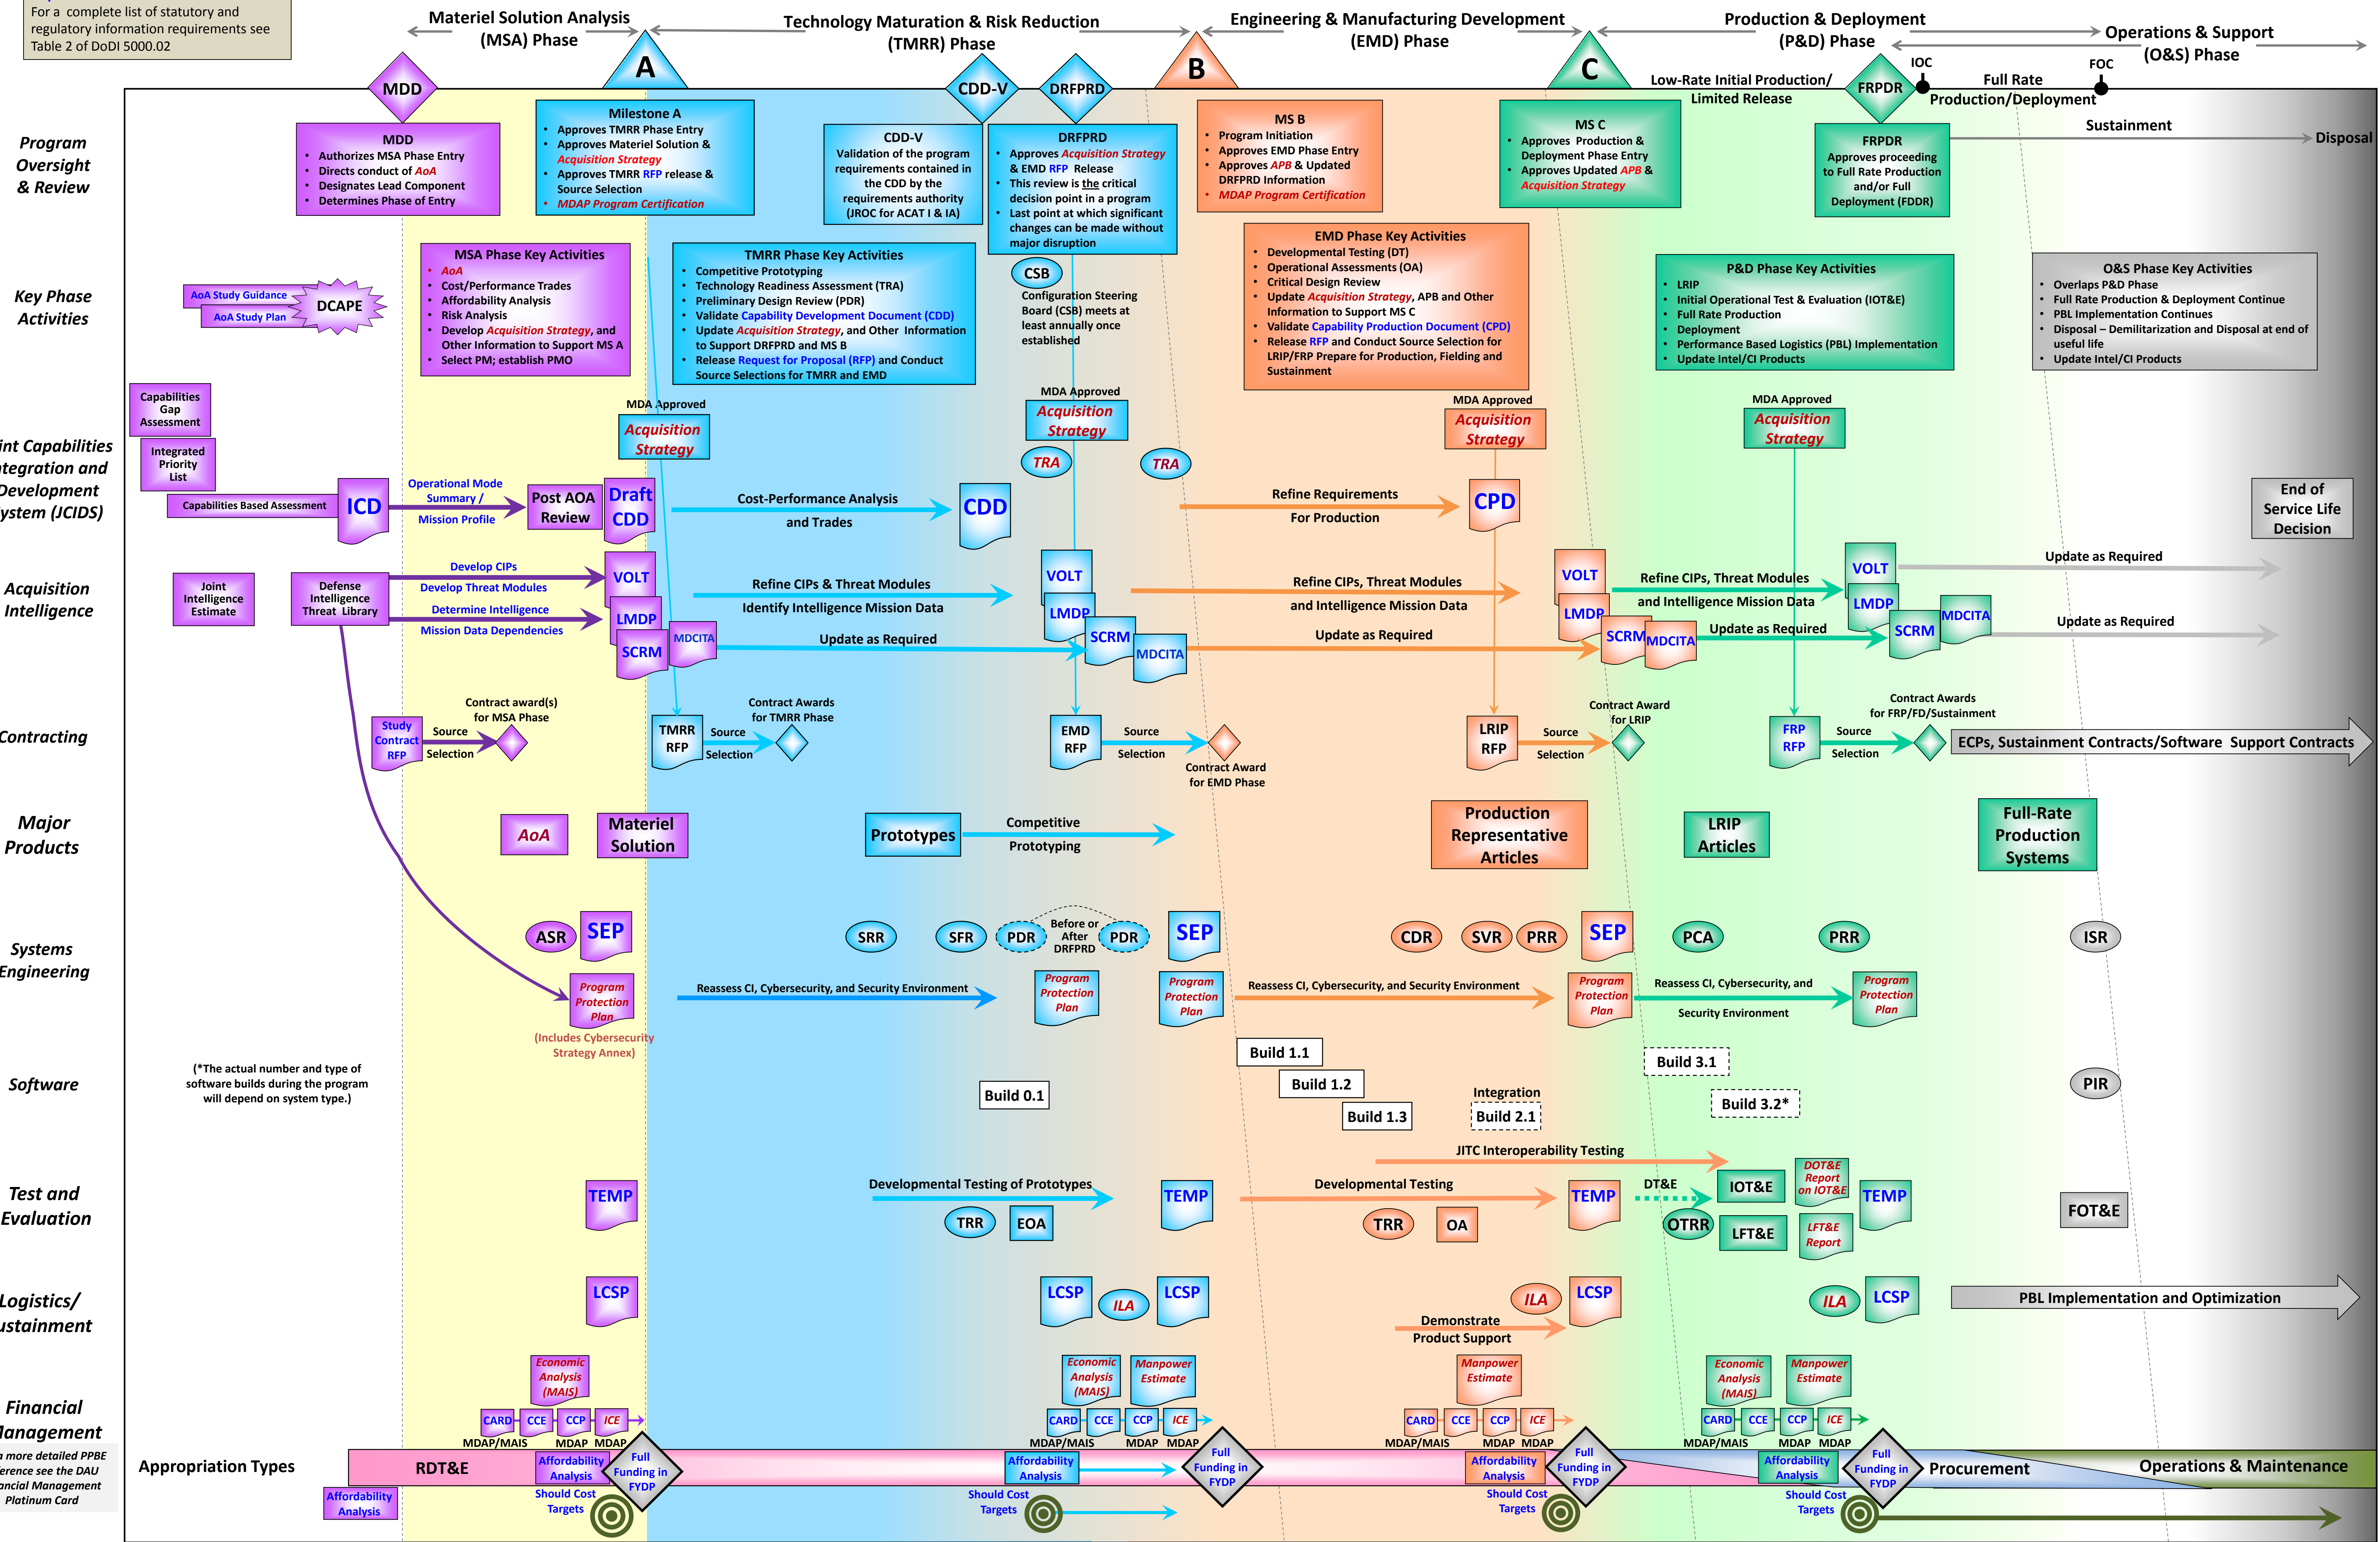

### Acronyms & Abbreviations

- ACAT – Acquisition Category
- AoA – Analysis of Alternatives
- APB – Acquisition Program Baseline
- ASR – Alternative Systems Review
- CARD – Cost Analysis Requirements Description
- CCE – Component Cost Estimate
- CCP – Component Cost Position
- CDD – Capability Development Document
- CDD-V – Capability Development Document Validation
- CDR – Critical Design Review
- CI – Counterintelligence
- CIPs – Critical Intelligence Parameters
- CPD – Capability Production Document
- CSB – Configuration Steering Board
- DCAPE – Director, Cost Assessment & Program Evaluation
- DRFRPD – Development Request for Proposals Release Decision
- DT&E – Developmental Test & Evaluation
- DoDI – Department of Defense Instruction
- DOT&E – Director of Operational Test & Evaluation
- ECPs – Engineering Change Proposals
- EMD – Engineering & Manufacturing Development
- EOA – Early Operational Assessment
- FCA – Functional Configuration Audit
- FD – Full Deployment
- FOC – Full Operational Capability
- FOT&E – Follow-on Operational Test & Evaluation
- FRP – Full-Rate Production
- FRP/FD – Full-Rate Production / Full Deployment Decision Review
- FYDP – Future Years Defense Program
- ICD – Initial Capabilities Document
- ICE – Independent Cost Estimate
- ILA – Independent Logistics Assessment
- IOC – Initial Operational Capability
- IOT&E – Initial Operational Test & Evaluation
- ISR – In-Service Review
- JITC – Joint Interoperability Test Command
- JROC – Joint Requirements Oversight Council
- LCCE – Life Cycle Cost Estimate
- LCSP – Life Cycle Sustainment Plan
- LFT&E – Live Fire Test & Evaluation
- LMDP – Life-Cycle Mission Data Plan
- LRIP – Low-Rate Initial Production
- MAIS – Major Automated Information System
- MDA – Milestone Decision Authority
- MDAP – Major Defense Acquisition Program
- MDCITA – Multi-Discipline Counterintelligence Threat Assessment
- MDD – Materiel Development Decision
- MS – Milestone
- MSA – Materiel Solution Analysis
- MS – Milestone
- OA – Operational Assessment
- OTRR – Operational Test Readiness Review
- PBL – Performance-Based Life-Cycle Product Support; Performance-Based Logistics
- PDR – Preliminary Design Review
- PIR – Post Implementation Review
- PM – Program Manager
- PMO – Program Management Office
- PPBE – Planning, Programming, Budgeting & Execution
- PRR – Production Readiness Review
- RDT&E – Research, Development, Test & Evaluation
- RFP – Request for Proposal
- SCRMP – Supply Chain Risk Management
- SEP – Systems Engineering Plan
- SRR – System Requirements Review
- SFR – System Functional Review
- SVR – System Verification Review
- TEMP – Test & Evaluation Master Plan
- TMRR – Technology Maturation & Risk Reduction
- TRA – Technology Readiness Assessment
- TRR – Test Readiness Review
- VOLT – Validated Online Lifecycle Threat

For a more detailed PPBE reference see the DAU Financial Management Platinum Card
